

Award of Construction Contract for Landscaping of US 101/Broadway Interchange



Background

- City of Burlingame sponsored the reconstruction of the US 101/Broadway Interchange
- Construction accepted by Caltrans in October 2018
- Landscaping suspended due to construction of the express lanes
- May 2024 MOU (TA and Burlingame) agreeing that the TA would manage the landscaping construction
- Landscaping is funded by prior Measure A allocation for the interchange
- Hired HDR to provide construction management and inspection services
















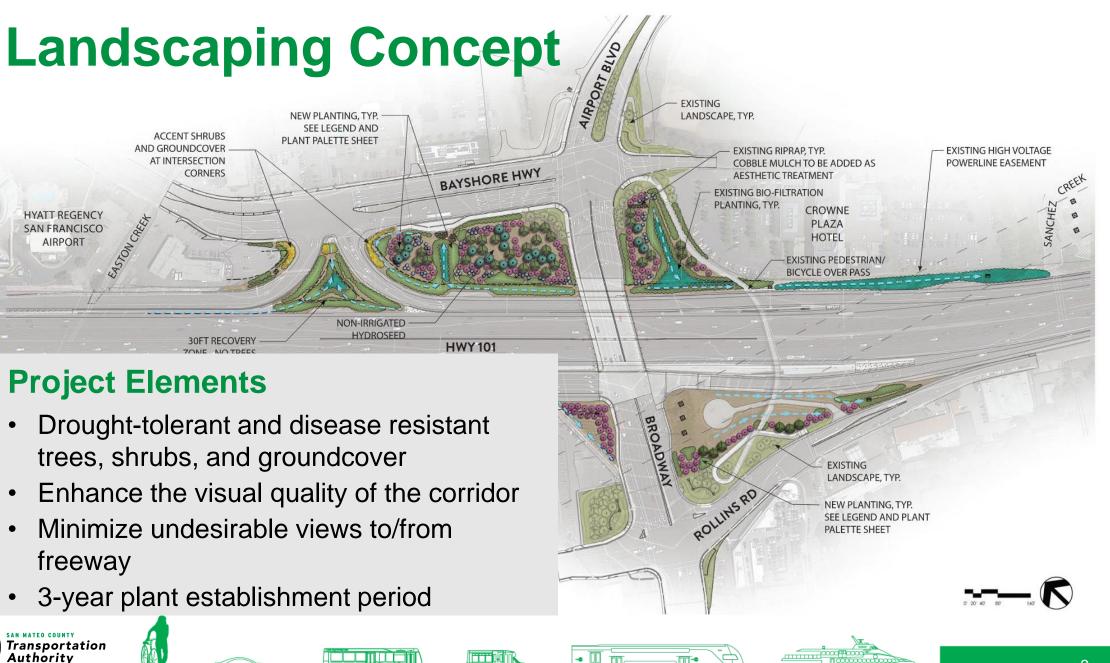

Procurement Process

- Issued an Invitation for Bids on August 7, 2024
- Pre-bid conference on August 14, 2024
- Received two bids on September 12, 2024

Company	Total Bid Price
Bortolussi & Watkin, Inc.	\$1,145,159
Marina Landscape, Inc.	\$1,250,612
Engineer's Estimate	\$1,689,620

 Lowest responsive bid and responsible bidder: Bortolussi & Watkin, Inc.











Next Steps

- Construction to start around March 2025
- 7-month construction period (until ~ October 2025)
- Plant establishment period for 3 years (until ~ October 2028)
- Assess pros and cons of TA serving as implementing agency for construction and document any lessons learned















Staff Recommendation

- Award a contract to the lowest, responsive and responsible bidder, Bortolussi & Watkin, Inc. of San Rafael, California (Bortolussi & Watkin), to provide Landscaping Construction of the US 101/Broadway Interchange Project (Project) for a grand total bid price of \$1,145,159, plus a contingency amount of up to ten percent of the Board awarded amount or \$250,000, whichever is greater, which the Executive Director or designee may use at their discretion for unforeseen work.
- Authorize the Executive Director or designee to execute a contract with Bortolussi & Watkin, Inc. in full conformity with the terms and conditions set forth in the solicitation documents and in a form approved by legal counsel.







